

HireHub — Sprint 2 Report

Project: HireHub — Intelligent Recruitment Platform

Sprint: 2

Review Date: 12-Nov-2025

1. Sprint Overview

Sprint 2 focused on enhancing account recovery, adding the Saved Jobs feature, developing the Employer Analytics Dashboard, enabling job application tracking, and activating employer notifications.

2. Team Roles and Responsibilities

Product Owner: Joud AlShahrani

- Defines the product vision and strategy
- Manages and prioritizes the Product Backlog
- Ensures clear communication of requirements to the development team
- Makes decisions about feature priority and acceptance criteria
- Represents stakeholder interests

Scrum Master: Jadel Alsaeri

- Facilitates all Scrum ceremonies
- Removes impediments and obstacles blocking the team
- Ensures adherence to Agile principles and Scrum framework
- Coaches the team on self-organization
- Protects the team from external interruptions

Frontend Developer: Albandri Alsadon

- Designs and develops responsive user interfaces
- Ensures optimal user experience and accessibility
- Implements frontend features and components

- Collaborates with backend developer for API integration
- Conducts frontend testing and debugging

Backend Developer: Ghada Altemyat

- Develops and maintains RESTful APIs
- Manages database design and optimization
- Ensures system security and data integrity
- Implements business logic and server-side functionality
- Optimizes application performance and reliability

3. Sprint Goal

Deliver secure account recovery, Saved Jobs feature, employer analytics, application tracking, and full notifications.

4. Completed User Stories

ID	As a...	I want...	So that...	Priority	Number of Stories	Current Status	Target Status
1	As a job seeker	I want to create an account using my email and password	so that I can access the platform and apply for jobs	High	1	Completed	Completed
2	As a registered user	I want to log into my account securely	so that I can access my personalized dashboard	High	1	Completed	Completed
3	As a user who forgot my password	I want to reset my password via email	so that I can regain access to my account	High	1	Completed	Completed
4	As a job seeker	I want to create and complete my professional profile	so that employers can view my qualifications	Medium	1	Completed	Completed
5	As a job seeker	I want to upload my resume in PDF or Word format	so that employers can download and review my full credentials	Medium	1	Not Started	Not Started
6	As a job seeker	I want to update my profile information at any time	so that my profile stays current and accurate	Low	2	Not Started	Not Started
7	As a job seeker	I want to search for jobs using keywords	so that I can find relevant opportunities quickly	High	1	Completed	Completed
8	As an employer	I want to view and filter applications by skills and experience	so that I can attract candidates efficiently	Medium	2	Not Started	Not Started
9	As an employer	I want to schedule interviews through the platform	so that communication with candidates is organized	Medium	2	Not Started	Not Started
10	As an employer	I want to create and publish job postings	so that I can attract qualified candidates	High	1	Not Started	Not Started
11	As an employer	I want to manage my account (name, password, email)	so that I can maintain platform quality and security	Low	2	Not Started	Not Started
12	As an admin	I want to view system usage reports and analytics	so that I can make data-driven decisions	Medium	2	Not Started	Not Started
13	As an admin	I want to manage user accounts (new, suspended, deleted)	so that I can maintain platform quality and security	Low	2	Not Started	Not Started
14	As an employer	I want to receive alerts when a new candidate applies	so that I can act promptly	Low	2	Not Started	Not Started
15	As a job seeker	I want to save jobs for later review	so that I can apply when ready	Medium	2	Not Started	Not Started
16	As a job seeker	I want to track the status of my job applications	so that I know where I stand in the hiring process	High	2	Not Started	Not Started
17	As an employer	I want to receive notifications when candidates apply to my jobs	so that I can respond promptly to new applications	Medium	2	Not Started	Not Started
3.1	As a user who forgot my password	I want to recover my account using email, phone number, or security questions		High	2	Not Started	Not Started

5. Acceptance Criteria Verification

All acceptance criteria were met, demonstrated, and validated by the Product Owner.

6. Work Demonstrated

Feature

Multi-method password recovery

Saved Jobs list and saving logic

Employer analytics with charts and statistics

Resume upload with file preview

Profile editing with validation

Applicant filtering system

Application status tracking

In-app and email-based notifications

7. Stakeholder Feedback

- Positive Feedback:
- Improved user experience
 - Better feature integration
 - Strong backend performance
- Suggested Enhancements:
- Clearer system messages
 - Better navigation flow
 - More consistent visuals

8. Progress & Impediments

Impediment	Resolution
Analytics performance issues	Database indexing applied
delivery delays	Queue-based processing implemented


9. Risks & Mitigation

Risk	Mitigation
Large dataset analytics	Optimized queries & indexing
File upload vulnerabilities	Strict file type validation
Notification overload	Queue-based message handling

10- SPRINT BACKLOG

SPRINT TRACKING				DAYS																									
User Stories and Tasks	ASSIGNED TO	ASSIGNED HOURS	HOURS USED	AVAILABLE HOURS PER DAY	DAY 1	DAY 2	DAY 3	DAY 4	DAY 5	DAY 6	DAY 7	DAY 8	DAY 9	DAY 10	DAY 11	DAY 12	DAY 13	DAY 14	DAY 15	DAY 16	DAY 17	DAY 18	DAY 19	DAY 20	DAY 21	DAY 22	DAY 23	DAY 24	
User Story US-005: Enhanced Password Recovery				8	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Task 1.1 Task Name: Design Password Recovery Details	Abdullah Alsaad	8	5	1	2	2	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.2 Implement Phone Number Verification	Ghada Alameyat	10	3	1	2	3	2	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.3 Create Security Questions System	Jadid Alsaad	8	0	0	2	2	2	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.4 Integrate SMS Service for OTP	Ghada Alameyat	8	8	0	3	2	1	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.5 Test All Recovery Methods	Jadid Alsaad	5	5	0	0	0	2	3	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
US-005 - New Job Feature				8	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Task 1.1 Design New Job Interface	Abdullah Alsaad	4	4	0	0	0	1	1	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.2 Create New Job Database Schema	Jadid Alsaad	4	6	0	0	0	0	0	3	3	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.3 Implement Search/Filter Functionality	Ghada Alameyat	8	8	0	0	0	0	0	2	2	3	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.4 Build Saved Jobs Dashboard Section	Abdullah Alsaad	8	0	0	0	0	0	0	0	3	2	2	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.5 Test New Job Feature	Ghada Alameyat	4	4	0	0	0	0	0	0	2	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
US-005 - Resume Upload				8	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Task 1.1 Design Resume Upload Interface	Abdullah Alsaad	5	5	0	0	0	0	0	0	2	2	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.2 Implement File Upload Functionality	Ghada Alameyat	8	7	1	0	0	0	0	0	2	2	3	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.3 Create File Storage System	Jadid Alsaad	7	7	0	0	0	0	0	0	2	3	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.4 Add Resume Preview Feature	Abdullah Alsaad	6	6	0	0	0	0	0	0	2	2	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.5 Test File Upload and Validation	Jadid Alsaad	4	4	0	0	0	0	0	0	2	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
US-006 - Profile Update				8	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Task 1.1 Design Edit Profile UI	Abdullah Alsaad	5	5	0	0	0	0	0	0	2	2	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.2 Implement Profile Update API	Jadid Alsaad	8	8	0	0	0	0	0	0	0	2	3	3	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.3 Add Form Validation	Ghada Alameyat	6	5	1	0	0	0	0	0	0	2	3	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.4 Test Profile Update Flow	Jadid Alsaad	4	3	1	0	0	0	0	0	0	1	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
US-006 - Application Filtering				8	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Task 1.1 Design Filter UI Components	Abdullah Alsaad	7	7	0	0	0	0	0	0	0	0	2	2	3	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.2 Implement Filter Logic	Jadid Alsaad	10	8	2	0	0	0	0	0	0	0	1	2	3	2	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.3 Create Filter API Endpoints	Ghada Alameyat	8	8	0	0	0	0	0	0	0	0	1	3	2	2	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.4 Test Filtering Functionality	Jadid Alsaad	5	5	0	0	0	0	0	0	0	0	2	2	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
US-010 - Job Application Tracking				8	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Task 1.1 Design Application Tracking Dashboard	Abdullah Alsaad	8	8	0	0	0	0	0	0	0	0	0	2	4	2	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.2 Create Application Status Database	Jadid Alsaad	7	7	0	0	0	0	0	0	0	0	2	2	3	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.3 Implement Status Update Logic	Ghada Alameyat	10	10	0	0	0	0	0	0	0	0	0	0	0	2	4	3	1	0	0	0	0	0	0	0	0	0	0	
Task 1.4 Build Timeline View Component	Abdullah Alsaad	8	7	1	0	0	0	0	0	0	0	0	0	0	2	2	3	0	0	0	0	0	0	0	0	0	0	0	
Task 1.5 Add Filter by Status Feature	Jadid Alsaad	6	6	0	0	0	0	0	0	0	0	0	0	0	2	2	0	0	0	0	0	0	0	0	0	0	0	0	
Task 1.6 Test Application Tracking System	Jadid Alsaad	5	5	0	0	0	0	0	0	0	0	0	0	0	3	2	0	0	0	0	0	0	0	0	0	0	0	0	
US-017 - Employee Notification System				7	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Task 1.1 Design Notification Center UI	Abdullah Alsaad	7	7	0	0	0	0	0	0	0	0	0	0	0	0	2	2	2	1	0	0	0	0	0	0	0	0	0	
Task 1.2 Create Notification Database Schema	Jadid Alsaad	6	6	0	0	0	0	0	0	0	0	0	0	0	0	1	1	2	2	0	0	0	0	0	0	0	0	0	
Task 1.3 Implement In-App Notification System	Ghada Alameyat	10	10	0	0	0	0	0	0	0	0	0	0	0	0	0	2	2	2	2	2	0	0	0	0	0	0	0	
Task 1.4 Integrate Email Notification Service	Ghada Alameyat	8	8	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	2	3	3	0	0	0	0	0	0	0	
Task 1.5 Build Notification Badge Component	Abdullah Alsaad	5	5	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	1	1	3	0	0	
Task 1.6 Add Mark as Read	Jadid Alsaad	6	5	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	3	1	1	0	0	

11- BurnDown CHART

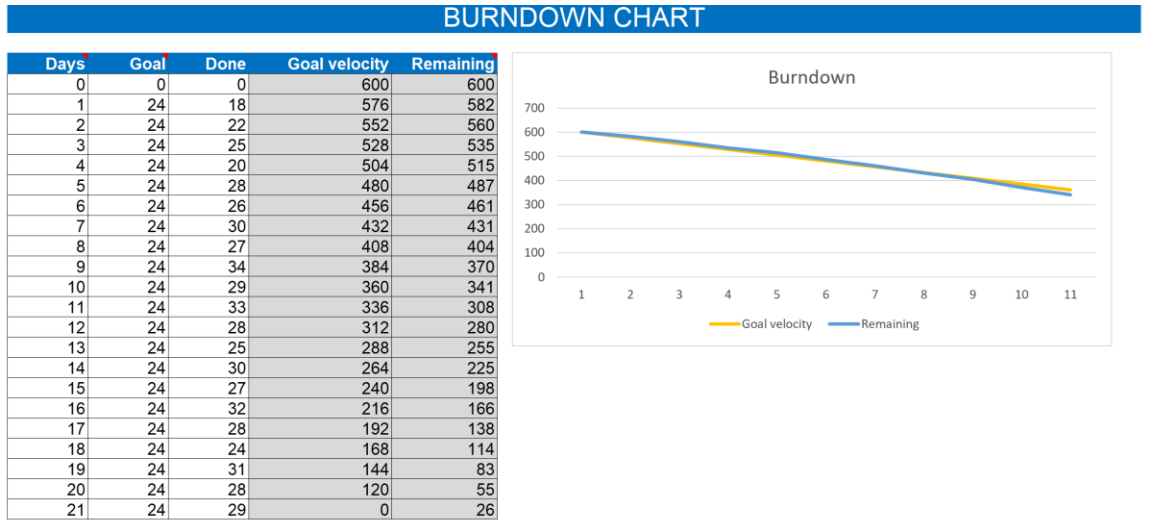

11- Sprint 2 Retrospective

Date:

Sprint 2 Retrospective

Meeting facilitator:

Loved What did you love? • Successful Completion of Ambitious Sprint • Effective Sprint Planning with New Stories • UI Consistency Improvements • Strong Cross-Team Collaboration • Successful SMS Integration	Learned What did you learn? • SMS API Integration • Email Notification Services • Real-Time System Architecture • Data Visualization Libraries • File Upload Security • Database Optimization • Component-Based Architecture
Lacked What did the team lack? • Automated Testing Coverage • SMS Service Documentation • Email Testing Environment • Performance Testing Tools • Mobile Testing Devices • Design System Documentation • Code Review Time	Longed for What did the team long for? • Continuous Integration/Deployment (CI/CD) • Dedicated QA Resource • Better Development Environment • Notification Testing Platform • Design Collaboration Tools • More Frequent Stakeholder Touchpoints • Knowledge Sharing Sessions

© 2022 Aha! Labs Inc.

13. Conclusion

Sprint 2 achieved all planned objectives, enhancing security, usability, analytics, application tracking, and notifications.

GitHub Link : <https://github.com/ladelsa/Agile-complete>

14. Meeting Attendance

Attendees

Joud AlShahrani

Jadel Alsaeri

Albandri Alsadon

Ghada Altemyat

Team member	Question	Sunday	Monday	Tuesday	Wednesday	Thursday
Joud	What did you do yesterday?	Break	Reviewed backlog items	Enhanced user profile page	Enhanced user profile page	Enhanced user profile page
	What are doing today?	Updated product backlog	Enhancing user profile page	Enhancing user profile page	Enhancing user profile page	Checked API performance
	Is there anything blocking you?	No blockers	No blockers	No blockers	No blockers	No blockers
Jadel	What did you do yesterday?	Break	Reviewed backlog items	Tested user profile functions	Tested user profile functions	Tested user profile functions
	What are doing today?	Updated product backlog	Testing user profile functions	Testing user profile functions	Testing user profile functions	Checked API performance
	Is there anything blocking you?	No blockers	No blockers	No blockers	No blockers	No blockers
Jadel	What did you do yesterday?	Break	Reviewed backlog items	Test user profile functions	Test user profile functions	Test user profile functions
	What are doing today?	Updated product backlog	Testing user profile functions	Testing user profile functions	Testing user profile functions	Checked API performance
	Is there anything blocking you?	No blockers	No blockers	No blockers	No blockers	No blockers
Ghada	What did you do yesterday?	Break	Reviewed backlog items	Test user profile functions	Test user profile functions	Test user profile functions
	What are doing today?	Updated product backlog	Testing user profile functions	Testing user profile functions	Testing user profile functions	Checked API performance
	Is there anything blocking you?	No blockers	No blockers	No blockers	No blockers	No blockers
Albandri	What did you do yesterday?	Break	Reviewed backlog items	Test user profile functions	Test user profile functions	Test user profile functions
	What are doing today?	Updated product backlog	Testing user profile functions	Testing user profile functions	Testing user profile functions	Checked API performance
	Is there anything blocking you?	No blockers	No blockers	No blockers	No blockers	No blockers

DAILY SCRUM						
Team member	Question	Sunday	Monday	Tuesday	Wednesday	Thursday
Joud	What did you do yesterday?	Break	Make sure we apply INVEST	Updated UI elements	Refined UI design	Refining design based on feedback
	What are doing today?	Make sure we apply INVEST	Updated UI elements	Refined UI design	Refining design based on feedback	Integrating API with frontend
	Is there anything blocking you?	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.
Jadel	What did you do yesterday?	Break	Make sure we apply INVEST	Updated UI elements	Refined UI design	Refining design based on feedback
	What are doing today?	Make sure we apply INVEST	Updated UI elements	Refined UI design	Refining design based on feedback	Integrating API with frontend
	Is there anything blocking you?	No major issues.	No major issues.	No major issues.	No major issues.	No major issues.
Ghada	What did you do yesterday?	Break	Make sure we apply INVEST	Updated UI elements	Refined UI design	Refining design based on feedback
	What are doing today?	Make sure we apply INVEST	Updated UI elements	Refined UI design	Refining design based on feedback	Integrating API with frontend
	Is there anything blocking you?	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.
Albandri	What did you do yesterday?	Break	Make sure we apply INVEST	Updated UI elements	Refined UI design	Refining design based on feedback
	What are doing today?	Make sure we apply INVEST	Updated UI elements	Refined UI design	Refining design based on feedback	Integrating API with frontend
	Is there anything blocking you?	No major issues.	No major issues.	No major issues.	No major issues.	No major issues.

DAILY SCRUM						
Team member	Question	Sunday	Monday	Tuesday	Wednesday	Thursday
Joud	What did you do yesterday?	Break	Tested navigation menu	Tested navigation menu	Tested navigation menu	Tested data flow
	What are doing today?	Enhancing navigation menu	Enhancing navigation menu	Test navigation menu	Test data flow	Completing documentation
	Is there anything blocking you?	No blockers	No blockers	No blockers	No blockers	No blockers
Jadel	What did you do yesterday?	Break	Enhanced navigation menu	Enhanced navigation menu	Tested navigation menu	Tested data flow
	What are doing today?	Enhancing navigation menu	Enhancing navigation menu	Test navigation menu	Test data flow	Completing documentation
	Is there anything blocking you?	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.
Ghada	What did you do yesterday?	Break	Enhanced database schema	Enhanced database schema	Tested database schema	Tested data flow
	What are doing today?	Enhancing database schema	Enhancing database schema	Test database schema	Test data flow	Completing documentation
	Is there anything blocking you?	Database problem	Database problem	Everything went smoothly.	Everything went smoothly.	Everything went smoothly.
Albandri	What did you do yesterday?	Break	Enhanced database schema	Enhanced database schema	Tested database schema	Tested data flow
	What are doing today?	Enhancing database schema	Enhancing database schema	Test database schema	Test data flow	Completing documentation
	Is there anything blocking you?	Database problem	Database problem	No blockers	No blockers	No blockers
